

# Santa Ana River - Mill Creek Cooperative Water Project

## Daily Flow Report Summary

Date: 7/5/2019

Time: 6:55:00 AM

Santa Ana River		Flow Rate (cfs)
<b>A5</b>	<b>Total SAR Inflows</b>	59.5
<b>N2</b>	<b>Total SAR Deliveries</b>	59.5
A1	SAR PH#3 Penstock (calc)	0.0
B1	BVMWC Highline	0.0
C1	Greenspot Pipeline	0.0
L2	SBVWCD Parshall Flume	29.0
G2	North Fork Canal Weir	5.6
H2	Edwards Canal	0.9
W1	Redlands Aqueduct (calc)	24.0
	Other	0.0

Mill Creek		Flow Rate (cfs)
<b>D3</b>	<b>Total MC Inflows</b>	25.0
<b>U3</b>	<b>Total MC Deliveries</b>	25.0
K3	Yucaipa Pipeline	0.0
O3	SBVWCD Spreading	9.0
T3	MC #1 Flow (Cooley Hat)	25.0

State Water Project		Flow Rate (cfs)
<b>G</b>	<b>Total SWP Inflows</b>	67.0
<b>V</b>	<b>Total SWP Deliveries</b>	67.0
J	Northfork Canal	0.0
L	Redlands Aqueduct	0.0
M	Crafton Unger Lane	0.0
T	Newport to BVMWC	0.0

Reservoir Levels	Feet
Observation at SOD	2161.1
Crafton Reservoir Level (21.3)	17.6
Mentone Reservoir Level	19.8

River Recharge	AF
Estimate SAR Recharge (AF)	0
Estimate Mill Creek Recharge (AF)	0
Estimated Total River Recharge (AF)	0

Location	Type	WY to Date (AF)	Target
Santa Ana River	SAR	32,412	176,000
Santa Ana River to Mill Creek	SAR-MC	267	0
Santa Ana River	SWP	8,645	0
Mill Creek	MC	9,254	106,000
Mill Creek	SWP	7,687	0
Redlands	SWP	0	0
Loma Linda	SWP	0	0
East Valley	SWP	134	0

Notes: Numbers on the Daily Flow Report are a snapshot of water at a given location at the time of the read, normally very early in the morning, and not necessarily what is at that location throughout the day.

# Santa Ana River - Mill Creek Cooperative Water Project

## Daily Flow Report

Date: 7/5/2019  
Time: 6:55:00 AM

### State Water Project

Inflows			Deliveries								
A	BBMWD In-lieu	5.0	H	EVWD City Creek	8.0	M	Crafton Unger Lane	0.0	S	SBCFCD Grove	0.0
B	Muni test at Greenspot Station	0.0	I	Santa Ana Low Turnout	20.5	N	BVMWC Boullioun Box	5.0	T	Newport for BVMWC	0.0
C	Exchange Water	0.0	J	Northfork Canal	0.0	P	SARC West	0.0	U	M/C spreading at Zanja Tate	33.5
D	Purchased Water	62.0	K	Edwards Canal	0.0	Q	Zanja	0.0	W	Tres Lagos	0.0
E	Redlands Aqueduct Leakage	0.0	L	Redlands Aqueduct	0.0	R	Tate Treatment Plant	0.0	V	<b>Total SWP Deliveries</b>	<b>67.0</b>
F	Recharge Project	0.0									
G	<b>Total SWP Inflows</b>	<b>67.0</b>									

### Santa Ana River Inflows

SAR PH #3 Penstock (calc)		BVMWC Highline		SOD Release Subtotal		Total SAR Inflows					
G2	Northfork Canal Weir	5.6	A2	Newport	0.0	D1	BVMWC River PU (USGS)	30.5	A1	SAR PH #3 Penstock (calc)	0.0
H2	Edwards Canal	0.9	D2	Boullioun Box Weir	0.0	E1	Main River Gage (USGS)	29.0	B1	BVMWC Highline	0.0
J2	Tailrace Valve to Parshall Flume	0.0	E2	Boullioun Box to Zanja	0.0	<b>minus</b>		C1	Greenspot Pipeline	0.0	
K2	Northfork Parshall Flume	0.0	F2	SBVWCD Mill Creek Spreading	0.0	F1	Greenspot Spill	0.0	D1	BVMWC River PU (USGS)	30.5
V1	PH#3 Afterbay SpillLoss to SAR	0.0	B1	<b>BVMWC Highline</b>	<b>0.0</b>	Z1	<b>SOD Release Subtotal</b>	<b>59.5</b>	E1	Main River Gage (USGS)	29.0
W1	Redlands Aqueduct / Sandbox	14.5	<b>Other</b>					D1a	BV Pick-Up gated	<input type="checkbox"/>	
Y1	Redlands Sandbox Spill	10.0	J1	Big Bear Lake Release	0.6	w	Observation at SOD	2161.1	A5	<b>Total SAR Inflows</b>	<b>59.5</b>
<b>minus</b>			L1	SCE SAR AVM (SCADA)	0.0	x	SOD Reservoir Elevation (scada)	2161.7	<b>Edison Generation</b>		
D1	BVMWC River PU (USGS)	30.5	X1	SAR-MC Spread (Red. Aqueduct)	0.0	y	Debris Pool Elevation	N/A	SAR PH#1 Generating	<input type="checkbox"/>	
I1	Redlands Tunnel	0.5						SAR PH#3 Generating	<input type="checkbox"/>		
A1	<b>SAR PH #3 Penstock (calc)</b>	<b>0.0</b>									
K1	<b>PH#3 Penstock (SCADA)</b>	<b>N/A</b>									

### Santa Ana River Deliveries

Greenspot Pipeline		Tailrace Pipeline		SBVWCD Parshall Flume To Basins		Deliveries					
M1	SBCFCD Grove	0.0	G2	Northfork Canal Weir	5.6	J2	Tailrace Valve to Parshall Flume	0.0	V1	SAR PH #3 Afterbay Spill	0.0
N1	BVMWC Highline	0.0	H2	Edwards Canal	0.9	K2	Northfork Parshall Flume	0.0	W1	Redlands Aqueduct / Sandbox	14.5
O1	Newport for BVMWC	0.0	J2	Tailrace Valve to Parshall Flume	0.0	H1	SBVWCD Diversion	29.0	Y1	Redlands Sandbox Spill	10.0
P1	SBVWCD Mill Creek Spreading	0.0	K2	Northfork Parshall Flume	0.0	<b>minus</b>		Z2	Cuttle Weir To River	0.0	
Q1	Crafton WC Unger Lane	0.0	I2	<b>Tailrace Pipeline</b>	<b>6.5</b>		Sedimentation Basin Recharge	0.0	B1	BVMWC Highline	0.0
R1	BVMWC Highline to Boullioun	0.0	<b>Irrigation</b>			L2	<b>SBVWCD Parshall Flume</b>	<b>29.0</b>	C1	Greenspot Pipeline	0.0
S1	Crafton WC Boullioun	0.0	D2	Boullioun Box Weir	0.0		<b>Parshall Flume (SCADA)</b>	<b>33.5</b>	I2	Tailrace Pipeline	6.5
T1	Tate Pump Station to Zanja	0.0	N	BVMWC Boullioun Box	5.0				L2	SBVWCD Parshall Flume	29.0
C1	<b>Greenspot Pipeline</b>	<b>0.0</b>	<b>minus</b>					<b>minus</b>			
			B2	Gay Overflow	4.0				J2	Tailrace Valve to Parshall Flume	0.0
			C2	<b>Irrigation</b>	<b>1.0</b>				K2	Northfork Parshall Flume	0.0
									I1	Redlands Tunnel	0.5
									N2	<b>Total SAR Deliveries</b>	<b>59.5</b>

### Mill Creek Inflows

Total MC Inflows		Other			
A3	RPU Flow	10.2	E3	M/C #1 Penstock Flow	25.0
B3	M/C #3 Penstock	14.8	F3	Stream Parshall Flume to Yucaipa	0.0
C3	SBVWCD Mill Creek Diversion	0.0	G3	Observation at Garnet	0.0
D3	<b>Total MC Inflows</b>	<b>25.0</b>			


### Mill Creek Deliveries

Yucaipa Pipeline		MC #1 Flow (Cooley Hat)		Total MC Deliveries		Other					
J3	Wilson Creek Spreading	0.0	P3	Tate Inflow	16.0	C3	SBVWCD Mill Creek Diversion	0.0	H3	Mentone Reservoir Level	19.8
K3	<b>Yucaipa Pipeline</b>	<b>0.0</b>	Q3	East Weir to Mill Creek	9.0	T3	Mill Creek #1 Flow (Cooley Hat)	25.0	R3	Boullioun to BVMWC Highline	0.0
			S3	East Weir to Zanja	0.0	U3	<b>Total MC Deliveries</b>	<b>25.0</b>	V3	Zanja West Weir to CWC Canal	0.0
			T3	<b>MC #1 Flow (Cooley Hat)</b>	<b>25.0</b>				W3	Mill Creek PH #2,3 Afterbay Spill	0.0
			N3	<b>Cooley Hat (SCADA)</b>	<b>29.6</b>				Y3	Crafton Reservoir Level (21.3)	17.6

### SBVWCD Recharge

Location	Type	Previous Day (AF)		WY To Date (AF)		Target	Calendar Year To Date (AF)		Target
A4	Santa Ana River	E4	119.0	I4	32,412.4	176,000	I4	32,341.5	176,000
M4	Santa Ana Rvr to Mill Creek	N4	0.0	O4	267.0		O4	175.5	
B4	Santa Ana River	F4	50.3	J4	8,645.2		J4	7,629.9	
C4	Mill Creek	G4	35.7	K4	9,254.3	106,000	K4	8,641.8	106,000
D4	Mill Creek	H4	134.9	L4	7,687.3		L4	7,687.3	
	Redlands		0.0		0.0			0.0	
	Loma Linda		0.0		0.0			0.0	
	East Valley		0.0		134.4			0.0	
SAR Passing Cuttle Weir (cfs)	0	Share of Lost SAR Flow	0	Estimate SAR flow (cfs)	0	Estimate SAR Recharge (AF)	0		
Mill Creek Passing Garnet (cfs)	0	Share of Lost Mill Creek Flow	0	Estimate Mill Creek flow (cfs)	0	Estimate Mill Creek Recharge (AF)	0		
Flow in the River Above Alabama	0	Flowing Beyond Alabama	0	Total River Flow (cfs)	0	Total River Recharge (AF)	0		

# Santa Ana River - Mill Creek Cooperative Water Project Mill Creek Stations

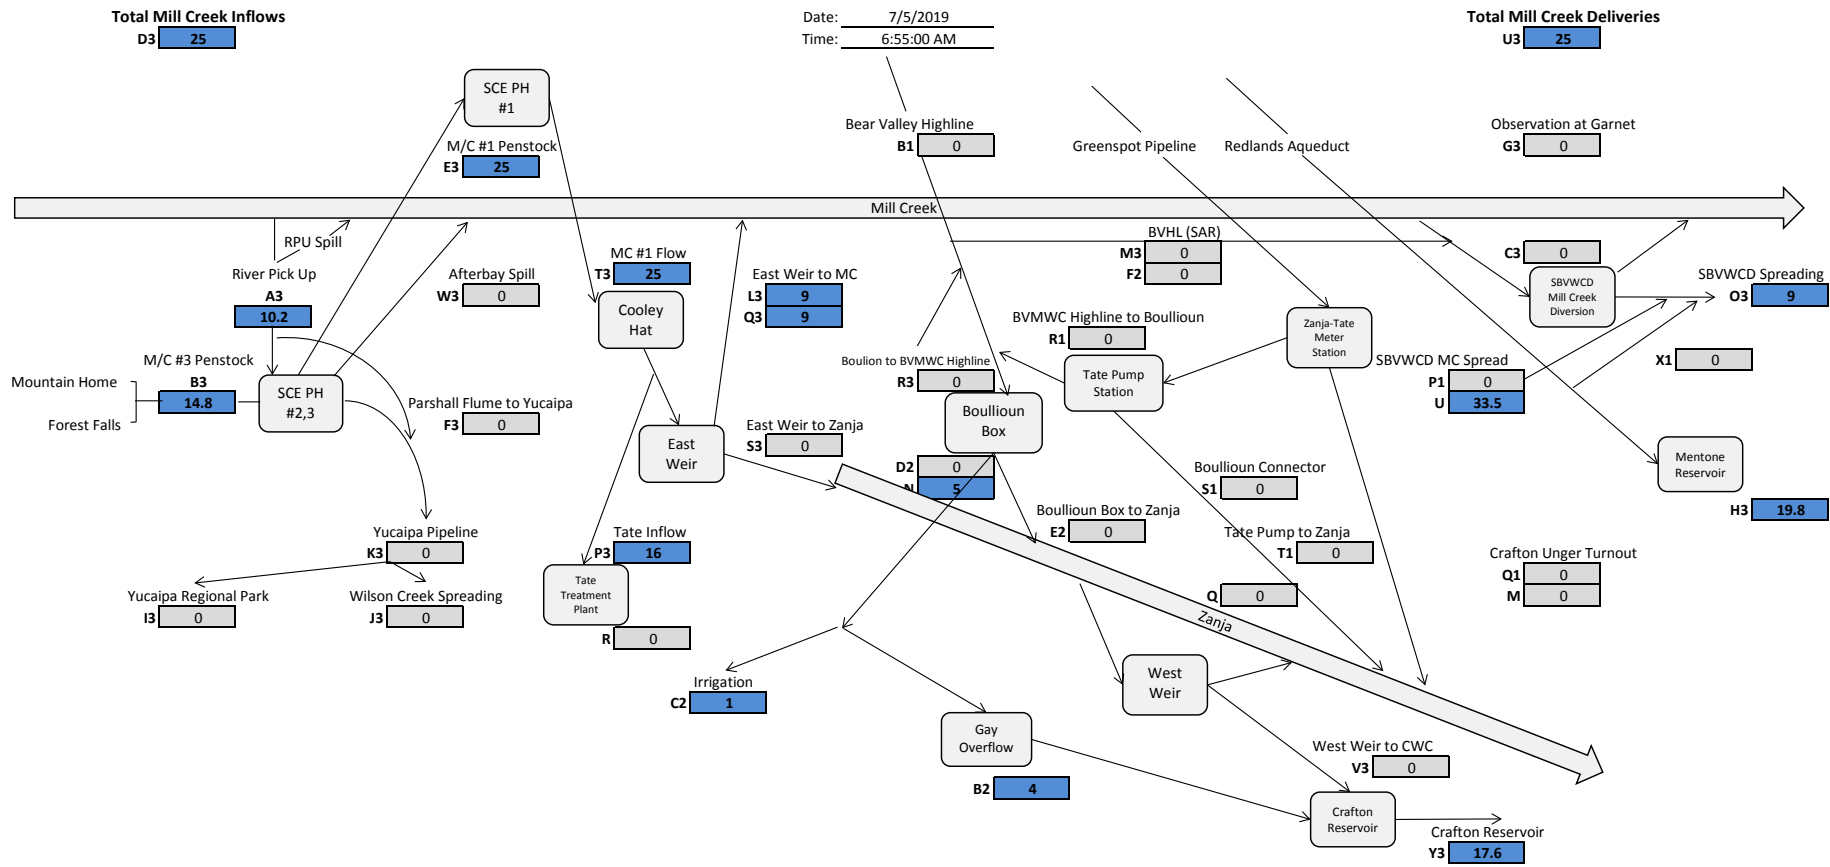

# Santa Ana River - Mill Creek Cooperative Water Project

## Santa Ana Stations

