

# Santa Ana River - Mill Creek Cooperative Water Project

## Daily Flow Report Summary

Date: 2/28/2018

Time: 6:50:00 AM

Santa Ana River		Flow Rate (cfs)
<b>A5</b>	<b>Total SAR Inflows</b>	29.9
<b>N2</b>	<b>Total SAR Deliveries</b>	29.9
A1	SAR PH#3 Penstock (calc)	0.0
B1	BVMWC Highline	3.5
C1	Greenspot Pipeline	0.0
L2	SBVWCD Parshall Flume	8.1
G2	North Fork Canal Weir	0.2
H2	Edwards Canal	0.0
W1	Redlands Aqueduct (calc)	18.1
	Other	0.0

State Water Project		Flow Rate (cfs)
<b>G</b>	<b>Total SWP Inflows</b>	5.3
<b>V</b>	<b>Total SWP Deliveries</b>	5.3
J	Northfork Canal	4.0
L	Redlands Aqueduct	0.0
M	Crafton Unger Lane	0.0
T	Newport to BVMWC	0.0

Location	Type
Santa Ana River	SAR
Santa Ana River to Mill Creek	SAR-MC
Santa Ana River	SWP
Mill Creek	MC
Mill Creek	SWP
Redlands	SWP
Loma Linda	SWP
East Valley	SWP

Mill Creek		Flow Rate (cfs)
<b>D3</b>	<b>Total MC Inflows</b>	14.5
<b>U3</b>	<b>Total MC Deliveries</b>	14.5
K3	Yucaipa Pipeline	0.0
O3	SBVWCD Spreading	2.0
T3	MC #1 Flow (Cooley Hat)	14.5

Reservoir Levels	Feet
Observation at SOD	2151.8
Crafton Reservoir Level (21.3)	16.8
Mentone Reservoir Level	21.2

River Recharge	AF
Estimate SAR Recharge (AF)	0
Estimate Mill Creek Recharge (AF)	0
Estimated Total River Recharge (AF)	0

Location	WY to Date (AF)	Target
Santa Ana River	549	166,000
Santa Ana River to Mill Creek	38	0
Santa Ana River	6,502	0
Mill Creek	987	99,700
Mill Creek	1,627	0
Redlands	0	0
Loma Linda	0	0
East Valley	0	0

Notes: Numbers on the Daily Flow Report are a snapshot of water at a given location at the time of the read, normally very early in the morning, and not necessarily what is at that location thruout the day.

# Santa Ana River - Mill Creek Cooperative Water Project

## Daily Flow Report

Date: 2/28/2018  
Time: 6:50:00 AM

State Water Project											
Inflows		Deliveries									
A	BBMWD In-lieu	1.3	H	EVWD City Creek	0.0	M	Crafton Unger Lane	0.0	S	SBCFCD Grove	0.0
B	Muni test at Greenspot Station	0.0	I	Santa Ana Low Turnout	0.0	N	BVMWC Boulliou Box	0.0	T	Newport for BVMWC	0.0
C	Exchange Water	0.0	J	Northfork Canal	4.0	P	SARC West	0.0	U	M/C spreading at Zanja Tate	0.0
D	Purchased Water	4.0	K	Edwards Canal	0.0	Q	Zanja	0.0	W	Tres Lagos	1.3
E	Redlands Aqueduct Leakage	0.0	L	Redlands Aqueduct	0.0	R	Tate Treatment Plant	0.0	V	<b>Total SWP Deliveries</b>	<b>5.3</b>
F	Recharge Project	0.0									
G	<b>Total SWP Inflows</b>	<b>5.3</b>									

Santa Ana River Inflows											
SAR PH #3 Penstock (calc)		BVMWC Highline		SOD Release Subtotal		Total SAR Inflows					
G2	Northfork Canal Weir	0.2	A2	Newport	0.0	D1	BVMWC River PU (USGS)	25.2	A1	SAR PH #3 Penstock (calc)	0.0
H2	Edwards Canal	0.0	D2	Boulliou Box Weir	3.5	E1	Main River Gage (USGS)	1.2	B1	BVMWC Highline	3.5
J2	Tailrace Valve to Parshall Flume	0.0	E2	Boulliou Box to Zanja	0.0	minus			C1	Greenspot Pipeline	0.0
K2	Northfork Parshall Flume	6.9	F2	SBVWCD Mill Creek Spreading	0.0	F1	Greenspot Spill	20.8	D1	BVMWC River PU (USGS)	25.2
V1	PH#3 Afterbay SpillLoss to SAR	0.0	B1	<b>BVMWC Highline</b>	<b>3.5</b>	Z1	<b>SOD Release Subtotal</b>	<b>5.6</b>	E1	Main River Gage (USGS)	1.2
W1	Redlands Aqueduct / Sandbox	18.4	Other						D1a	BV Pick-Up gated	<input type="checkbox"/>
Y1	Redlands Sandbox Spill	0.0	J1	Big Bear Lake Release	1.2	w	Observation at SOD	2151.8	A5	<b>Total SAR Inflows</b>	<b>29.9</b>
minus			L1	SCE SAR AVM (SCADA)	23.6	x	SOD Reservoir Elevation (scada)	2152.3	Edison Generation		
D1	BVMWC River PU (USGS)	25.2	X1	SAR-MC Spread (Red. Aqueduct)	0.0	y	Debris Pool Elevation	N/A	SAR PH#1 Generating	<input checked="" type="checkbox"/>	
I1	Redlands Tunnel	0.3							SAR PH#3 Generating	<input type="checkbox"/>	
A1	<b>SAR PH #3 Penstock (calc)</b>	<b>0.0</b>									
K1	<b>PH3# Penstock (SCADA)</b>	<b>0.0</b>									

Santa Ana River Deliveries											
Greenspot Pipeline		Tailrace Pipeline		SBVWCD Parshall Flume To Basins		Deliveries					
M1	SBCFCD Grove	0.0	G2	Northfork Canal Weir	0.2	J2	Tailrace Valve to Parshall Flume	0.0	V1	SAR PH #3 Afterbay Spill	0.0
N1	BVMWC Highline	0.0	H2	Edwards Canal	0.0	K2	Northfork Parshall Flume	6.9	W1	Redlands Aqueduct / Sandbox	18.4
O1	Newport for BVMWC	0.0	J2	Tailrace Valve to Parshall Flume	0.0	H1	SBVWCD Diversion	1.2	Y1	Redlands Sandbox Spill	0.0
P1	SBVWCD Mill Creek Spreading	0.0	K2	Northfork Parshall Flume	6.9	L2	<b>SBVWCD Parshall Flume</b>	<b>8.1</b>	Z2	Cuttle Weir To River	0.0
Q1	Crafton WC Unger Lane	0.0	I2	<b>Tailrace Pipeline</b>	<b>7.1</b>	B1	<b>Parshall Flume (SCADA)</b>	<b>8.1</b>	B1	BVMWC Highline	3.5
R1	BVMWC Highline to Boulliou	0.0				Irrigation			C1	Greenspot Pipeline	0.0
S1	Crafton WC Boulliou	0.0				D2	Boulliou Box Weir	3.5	I2	Tailrace Pipeline	7.1
T1	Tate Pump Station to Zanja	0.0				minus			L2	SBVWCD Parshall Flume	8.1
C1	<b>Greenspot Pipeline</b>	<b>0.0</b>				B2	Gay Overflow	2.3	minus		
						C2	<b>Irrigation</b>	<b>1.2</b>	J2	Tailrace Valve to Parshall Flume	0.0
									K2	Northfork Parshall Flume	6.9
									I1	Redlands Tunnel	0.3
									N2	<b>Total SAR Deliveries</b>	<b>29.9</b>


Mill Creek Inflows					
Total MC Inflows		Other			
A3	RPU Flow	6.4	E3	M/C #1 Penstock Flow	14.5
B3	M/C #3 Penstock	8.1	F3	Stream Parshall Flume to Yucaipa	0.0
C3	SBVWCD Mill Creek Diversion	0.0	G3	Observation at Garnet	0.0
D3	<b>Total MC Inflows</b>	<b>14.5</b>			

Mill Creek Deliveries											
Yucaipa Pipeline		MC #1 Flow (Cooley Hat)		Total MC Deliveries		Other					
I3	Yucaipa Regional Park	0.0	P3	Tate Inflow	12.5	C3	SBVWCD Mill Creek Diversion	0.0	H3	Mentone Reservoir Level	21.2
J3	Wilson Creek Spreading	0.0	Q3	East Weir to Mill Creek	2.0	T3	Mill Creek #1 Flow (Cooley Hat)	14.5	R3	Boulliou to BVMWC Highline	0.0
K3	<b>Yucaipa Pipeline</b>	<b>0.0</b>	S3	East Weir to Zanja	0.0	W3	Mill Creek PH #2,3 Afterbay Spill	0.0	V3	Zanja West Weir to CWC Canal	0.0
			T3	<b>MC #1 Flow (Cooley Hat)</b>	<b>14.5</b>	U3	<b>Total MC Deliveries</b>	<b>14.5</b>	W3	Mill Creek PH #2,3 Afterbay Spill	0.0
			N3	<b>Cooley Hat (SCADA)</b>	<b>13.1</b>				Y3	Crafton Reservoir Level (21.3)	16.8

SBVWCD MC Spreading		
C3	SBVWCD Mill Creek Diversion	0.0
L3	East Weir (MC)	2.0
M3	BVHL (SAR)	0.0
W3	Mill Creek PH #2,3 Afterbay Spill	0.0
X1	SAR-MC Spread (Red. Aqueduct)	0.0
O3	<b>SBVWCD MC Spreading</b>	<b>2.0</b>

SBVWCD Recharge							
Location	Type	Previous Day (AF)	WY To Date (AF)	Target	Calendar Year To Date (AF)	Target	
A4	Santa Ana River	15.3	I4	548.9	166,000	I4	548.9
M4	Santa Ana Rvr to Mill Creek	0.0	O4	37.6		O4	11.3
B4	Santa Ana River	0.0	J4	6,502.3		J4	100.9
C4	Mill Creek	4.6	K4	986.5	99,700	K4	773.1
D4	Mill Creek	0.0	L4	1,627.4		L4	434.1
	Redlands	0.0		0.0			0.0
	Loma Linda	0.0		0.0			0.0
	East Valley	0.0		0.0			0.0
SAR Passing Cuttle Weir (cfs)	0	Share of Lost SAR Flow	0	Estimate SAR flow (cfs)	0	Estimate SAR Recharge (AF)	0
Mill Creek Passing Garnet (cfs)	0	Share of Lost Mill Creek Flow	0	Estimate Mill Creek flow (cfs)	0	Estimate Mill Creek Recharge (AF)	0
Flow in the River Above Alabama	0	Flowing Beyond Alabama	0	Total River Flow (cfs)	0	Total River Recharge (AF)	0

# Santa Ana River - Mill Creek Cooperative Water Project Mill Creek Stations

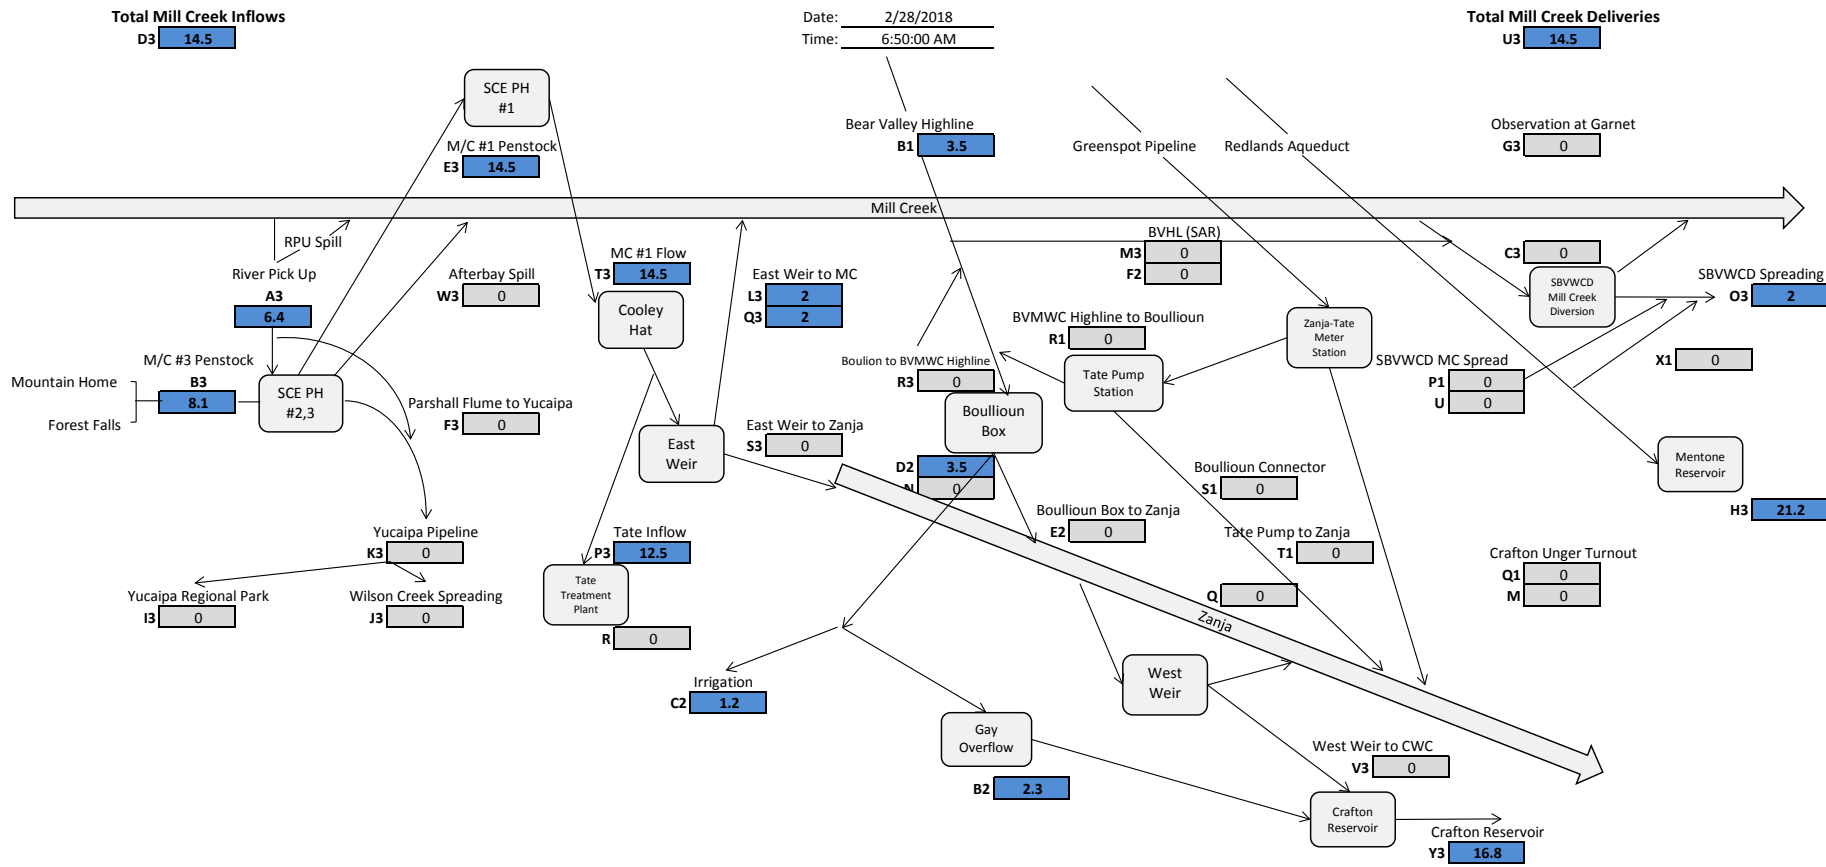

# Santa Ana River - Mill Creek Cooperative Water Project

## Santa Ana Stations

