

Santa Ana River - Mill Creek Cooperative Water Project

Daily Flow Report Summary

Date: 7/10/2018

Time: 6:40:00 AM

Santa Ana River		Flow Rate (cfs)
A5	Total SAR Inflows	9.5
N2	Total SAR Deliveries	9.5
A1	SAR PH#3 Penstock (calc)	6.8
B1	BVMWC Highline	1.3
C1	Greenspot Pipeline	0.0
L2	SBVWCD Parshall Flume	0.0
G2	North Fork Canal Weir	5.4
H2	Edwards Canal	0.9
W1	Redlands Aqueduct (calc)	1.9
	Other	0.0

State Water Project		Flow Rate (cfs)
G	Total SWP Inflows	38.4
V	Total SWP Deliveries	38.4
J	Northfork Canal	3.0
L	Redlands Aqueduct	13.0
M	Crafton Unger Lane	9.8
T	Newport to BVMWC	0.7

Location	Type
Santa Ana River	SAR
Santa Ana River to Mill Creek	SAR-MC
Santa Ana River	SWP
Mill Creek	MC
Mill Creek	SWP
Redlands	SWP
Loma Linda	SWP
East Valley	SWP

Mill Creek		Flow Rate (cfs)
D3	Total MC Inflows	10.6
U3	Total MC Deliveries	10.6
K3	Yucaipa Pipeline	0.0
O3	SBVWCD Spreading	4.0
T3	MC #1 Flow (Cooley Hat)	6.6


Reservoir Levels	Feet
Observation at SOD	N/A
Crafton Reservoir Level (21.3)	11.1
Mentone Reservoir Level	19.9

River Recharge	AF
Estimate SAR Recharge (AF)	0
Estimate Mill Creek Recharge (AF)	0
Estimated Total River Recharge (AF)	0

Location	Type	WY to Date (AF)	Target
Santa Ana River	SAR	2,387	166,000
Santa Ana River to Mill Creek	SAR-MC	115	0
Santa Ana River	SWP	6,502	0
Mill Creek	MC	1,508	99,700
Mill Creek	SWP	1,627	0
Redlands	SWP	0	0
Loma Linda	SWP	0	0
East Valley	SWP	128	0

Notes: Numbers on the Daily Flow Report are a snapshot of water at a given location at the time of the read, normally very early in the morning, and not necessarily what is at that location thruout the day.

Santa Ana River - Mill Creek Cooperative Water Project Mill Creek Stations

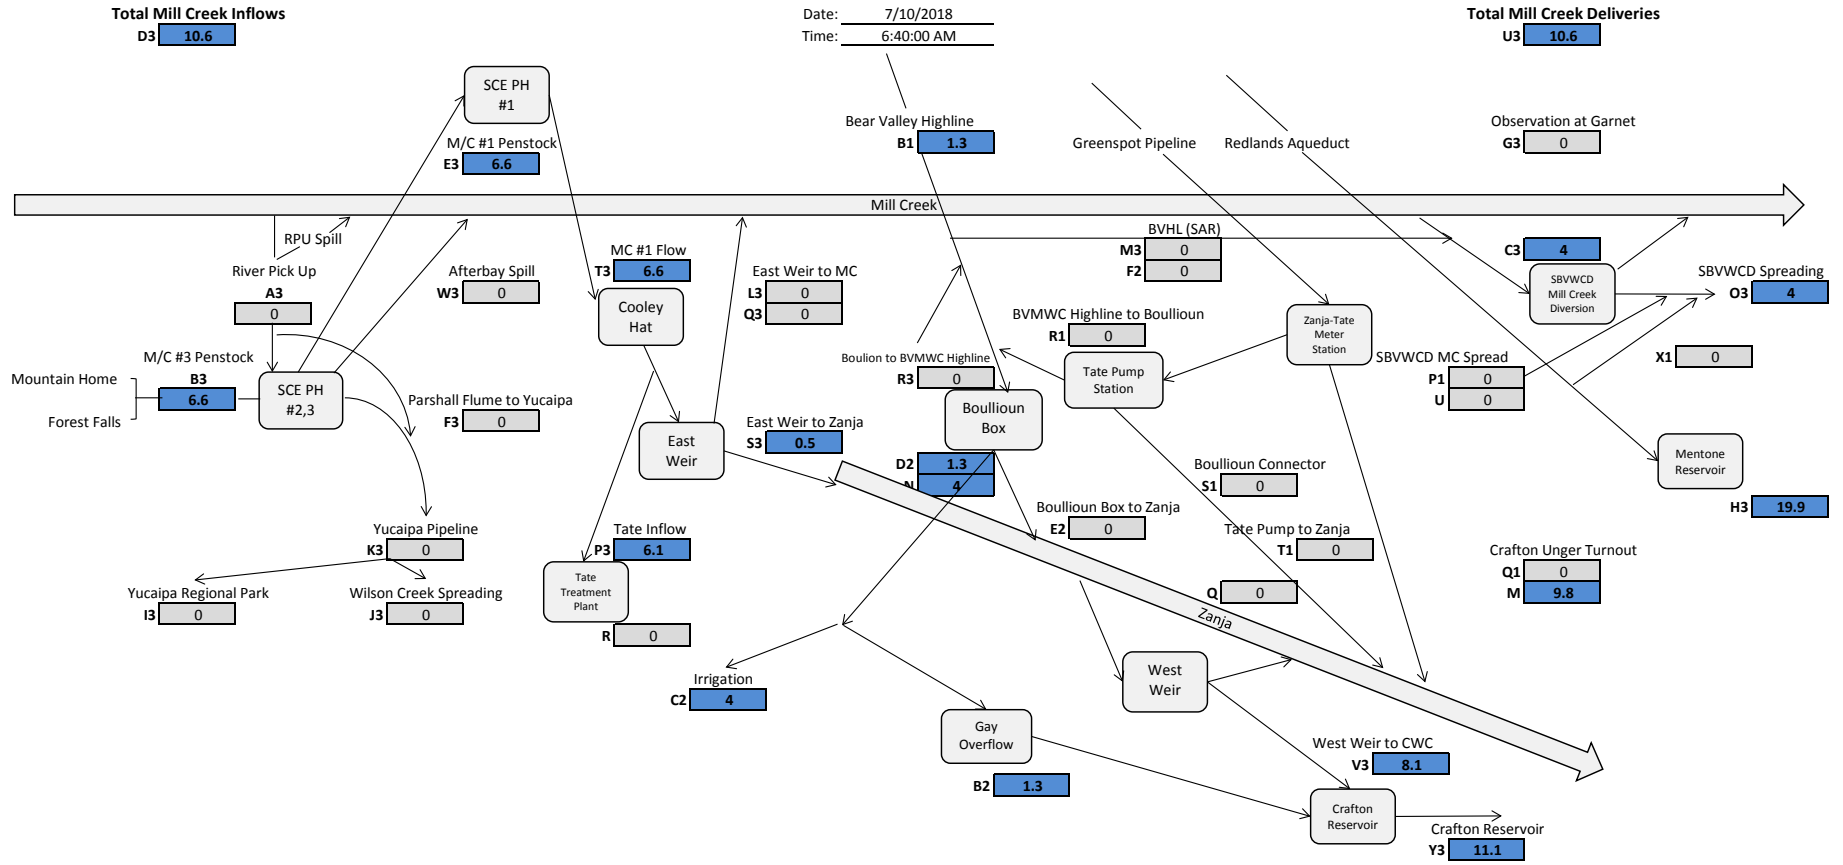

Santa Ana River - Mill Creek Cooperative Water Project

Santa Ana Stations

