

Santa Ana River - Mill Creek Cooperative Water Project

Daily Flow Report Summary

Date: 3/13/2020

Time: 6:30:00 AM

Santa Ana River		Flow Rate (cfs)
A5	Total SAR Inflows	7.7
N2	Total SAR Deliveries	7.7
A1	SAR PH#3 Penstock (calc)	0.0
B1	BVMWC Highline	3.6
C1	Greenspot Pipeline	0.0
L2	SBVWCD Parshall Flume	0.0
G2	North Fork Canal Weir	2.0
H2	Edwards Canal	0.0
W1	Redlands Aqueduct (calc)	2.1
	Other	0.0

State Water Project		Flow Rate (cfs)
G	Total SWP Inflows	14.0
V	Total SWP Deliveries	14.0
J	Northfork Canal	0.0
L	Redlands Aqueduct	10.0
M	Crafton Unger Lane	0.0
T	Newport to BVMWC	0.0

Mill Creek		Flow Rate (cfs)
D3	Total MC Inflows	22.0
U3	Total MC Deliveries	22.0
K3	Yucaipa Pipeline	0.0
O3	SBVWCD Spreading	0.0
T3	MC #1 Flow (Cooley Hat)	16.0

Reservoir Levels	Feet
Observation at SOD	2192.7
Crafton Reservoir Level (21.3)	19.3
Mentone Reservoir Level	21.8

River Recharge	AF
Estimate SAR Recharge (AF)	0
Estimate Mill Creek Recharge (AF)	20
Estimated Total River Recharge (AF)	20

Location	Type	WY to Date (AF)	Target
Santa Ana River	SAR	2,782	105,000
Santa Ana River to Mill Creek	SAR-MC	1,242	0
Santa Ana River	SWP	3,890	0
Mill Creek	MC	2,465	63,000
Mill Creek	SWP	3,251	0
Redlands	SWP	0	0
Loma Linda	SWP	0	0
East Valley	SWP	0	0

Notes: Numbers on the Daily Flow Report are a snapshot of water at a given location at the time of the read, normally very early in the morning, and not necessarily what is at that location throughout the day.

Santa Ana River - Mill Creek Cooperative Water Project

Daily Flow Report

Date: 3/13/2020
Time: 6:30:00 AM

State Water Project

Inflows			Deliveries								
A	BBMWD In-lieu	0.0	H	EVWD City Creek	4.0	M	Crafton Unger Lane	0.0	S	SBCFCD Grove	0.0
B	Muni test at Greenspot Station	0.0	I	Santa Ana Low Turnout	0.0	N	BVMWC Boullioun Box	0.0	T	Newport for BVMWC	0.0
C	Exchange Water	0.0	J	Northfork Canal	0.0	P	SARC West	0.0	U	M/C spreading at Zanja Tate	0.0
D	Purchased Water	14.0	K	Edwards Canal	0.0	Q	Zanja	0.0	W	Tres Lagos	0.0
E	Redlands Aqueduct Leakage	0.0	L	Redlands Aqueduct	10.0	R	Tate Treatment Plant	0.0	V	Total SWP Deliveries 14.0	
F	Recharge Project	0.0									
G	Total SWP Inflows	14.0									

Santa Ana River Inflows

SAR PH #3 Penstock (calc)			BVMWC Highline			SOD Release Subtotal			Total SAR Inflows		
G2	Northfork Canal Weir	2.0	A2	Newport	0.0	D1	BVMWC River PU (USGS)	4.1	A1	SAR PH #3 Penstock (calc)	0.0
H2	Edwards Canal	0.0	D2	Boullioun Box Weir	3.6	E1	Main River Gage (USGS)	0.0	B1	BVMWC Highline	3.6
J2	Tailrace Valve to Parshall Flume	0.0	E2	Boullioun Box to Zanja	0.0	minus			C1	Greenspot Pipeline	0.0
K2	Northfork Parshall Flume	0.0	F2	SBVWCD Mill Creek Spreading	0.0	F1	Greenspot Spill	0.0	D1	BVMWC River PU (USGS)	4.1
V1	PH#3 Afterbay SpillLoss to SAR	0.0	B1	BVMWC Highline	3.6	Z1	SOD Release Subtotal	4.1	E1	Main River Gage (USGS)	0.0
W1	Redlands Aqueduct / Sandbox	2.3							D1a	BV Pick-Up gated	☐
Y1	Redlands Sandbox Spill	0.0							A5	Total SAR Inflows	7.7
			Other								
D1	BVMWC River PU (USGS)	4.1	J1	Big Bear Lake Release	0.5	W	Observation at SOD	2192.7			
I1	Redlands Tunnel	0.2	L1	SCE SAR AVM (SCADA)	0.0	X	SOD Reservoir Elevation (scada)	N/A			
A1	SAR PH #3 Penstock (calc)	0.0	X1	SAR-MC Spread (Red. Aqueduct)	0.0	Y	Debris Pool Elevation	N/A			
K1	PH3# Penstock (SCADA)	NA									

Edison Generation	
SAR PH#1 Generating	☒
SAR PH#3 Generating	☐

Santa Ana River Deliveries

Greenspot Pipeline			Tailrace Pipeline			SBVWCD Parshall FlumeTo Basins			Deliveries		
M1	SBCFCD Grove	0.0	G2	Northfork Canal Weir	2.0	J2	Tailrace Valve to Parshall Flume	0.0	V1	SAR PH #3 Afterbay Spill	0.0
N1	BVMWC Highline	0.0	H2	Edwards Canal	0.0	K2	Northfork Parshall Flume	0.0	W1	Redlands Aqueduct / Sandbox	2.3
O1	Newport for BVMWC	0.0	J2	Tailrace Valve to Parshall Flume	0.0	H1	SBVWCD Diversion	0.0	Y1	Redlands Sandbox Spill	0.0
P1	SBVWCD Mill Creek Spreading	0.0	K2	Northfork Parshall Flume	0.0	minus			Z2	Cuttle Weir To River	0.0
Q1	Crafton WC Unger Lane	0.0	I2	Tailrace Pipeline	2.0		Sedimentation Basin Recharge	0.0	B1	BVMWC Highline	3.6
R1	BVMWC Highline to Boullioun	0.0				L2	SBVWCD Parshall Flume	0.0	C1	Greenspot Pipeline	0.0
S1	Crafton WC Boullioun	0.0	Irrigation				Parshall Flume (SCADA)	0.0	I2	Tailrace Pipeline	2.0
T1	Tate Pump Station to Zanja	0.0	D2	Boullioun Box Weir	3.6				L2	SBVWCD Parshall Flume	0.0
C1	Greenspot Pipeline	0.0	N	BVMWC Boullioun Box	0.0				minus		
									J2	Tailrace Valve to Parshall Flume	0.0
									K2	Northfork Parshall Flume	0.0
									I1	Redlands Tunnel	0.2
									N2	Total SAR Deliveries	7.7

Mill Creek Inflows

Total MC Inflows			Other		
A3	RPU Flow	0.0	E3	M/C #1 Penstock Flow	16.0
B3	M/C #3 Penstock	16.0	F3	Stream Parshall Flume to Yucaipa	0.0
C3	SBVWCD Mill Creek Diversion	6.0	G3	Observation at Garnet	15.0
D3	Total MC Inflows	22.0			

Mill Creek Deliveries

Yucaipa Pipeline			MC #1 Flow (Cooley Hat)			Total MC Deliveries			Other		
	Yucaipa Regional Park	0.0	P3	Tate Inflow	0.0	C3	SBVWCD Mill Creek Diversion	6.0	H3	Mentone Reservoir Level	21.8
J3	Wilson Creek Spreading	0.0	Q3	East Weir to Mill Creek	16.0	T3	Mill Creek #1 Flow (Cooley Hat)	16.0	R3	Boullioun to BVMWC Highline	0.0
K3	Yucaipa Pipeline	0.0	S3	East Weir to Zanja	0.0	U3	Total MC Deliveries	22.0	V3	Zanja West Weir to CWC Canal	0.0
			T3	MC #1 Flow (Cooley Hat)	16.0				W3	Mill Creek PH #2,3 Afterbay Spill	0.0
			N3	Cooley Hat (SCADA)	17.4				Y3	Crafton Reservoir Level (21.3)	19.3


SBVWCD MC Spreading		
C3	SBVWCD Mill Creek Diversion	0.0
L3	East Weir (MC)	0.0
M3	BVHL (SAR)	0.0
X1	SAR-MC Spread (Red. Aqueduct)	0.0
O3	SBVWCD MC Spreading	0.0

SBVWCD Recharge

Location	Type	Previous Day (AF)		WY To Date (AF)		Target	Calendar Year To Date (AF)		Target
A4	Santa Ana River	E4	0.0	I4	2,782.3	105,000	I4	321.4	105,000
M4	Santa Ana Rvr to Mill Creek	N4	0.0	O4	1,242.3		O4	880.9	
B4	Santa Ana River	F4	0.0	J4	3,890.4		J4	0.0	
C4	Mill Creek	G4	13.1	K4	2,464.8	63,000	K4	1,280.9	63,000
D4	Mill Creek	H4	0.0	L4	3,251.4		L4	161.2	
	Redlands		0.0		0.0			0.0	
	Loma Linda		0.0		0.0			0.0	
	East Valley		0.0		0.0			0.0	
SAR Passing Cuttle Weir (cfs)	0	Share of Lost SAR Flow	0	Estimate SAR flow (cfs)	0	Estimate SAR Recharge (AF)	0		
Mill Creek Passing Garnet (cfs)	15	Share of Lost Mill Creek Flow	0	Estimate Mill Creek flow (cfs)	15	Estimate Mill Creek Recharge (AF)	20		
Flow in the River Above Alabama	15	Flowing Beyond Alabama	0	Total River Flow (cfs)	15	Total River Recharge (AF)	20		

Santa Ana River - Mill Creek Cooperative Water Project

Mill Creek Stations

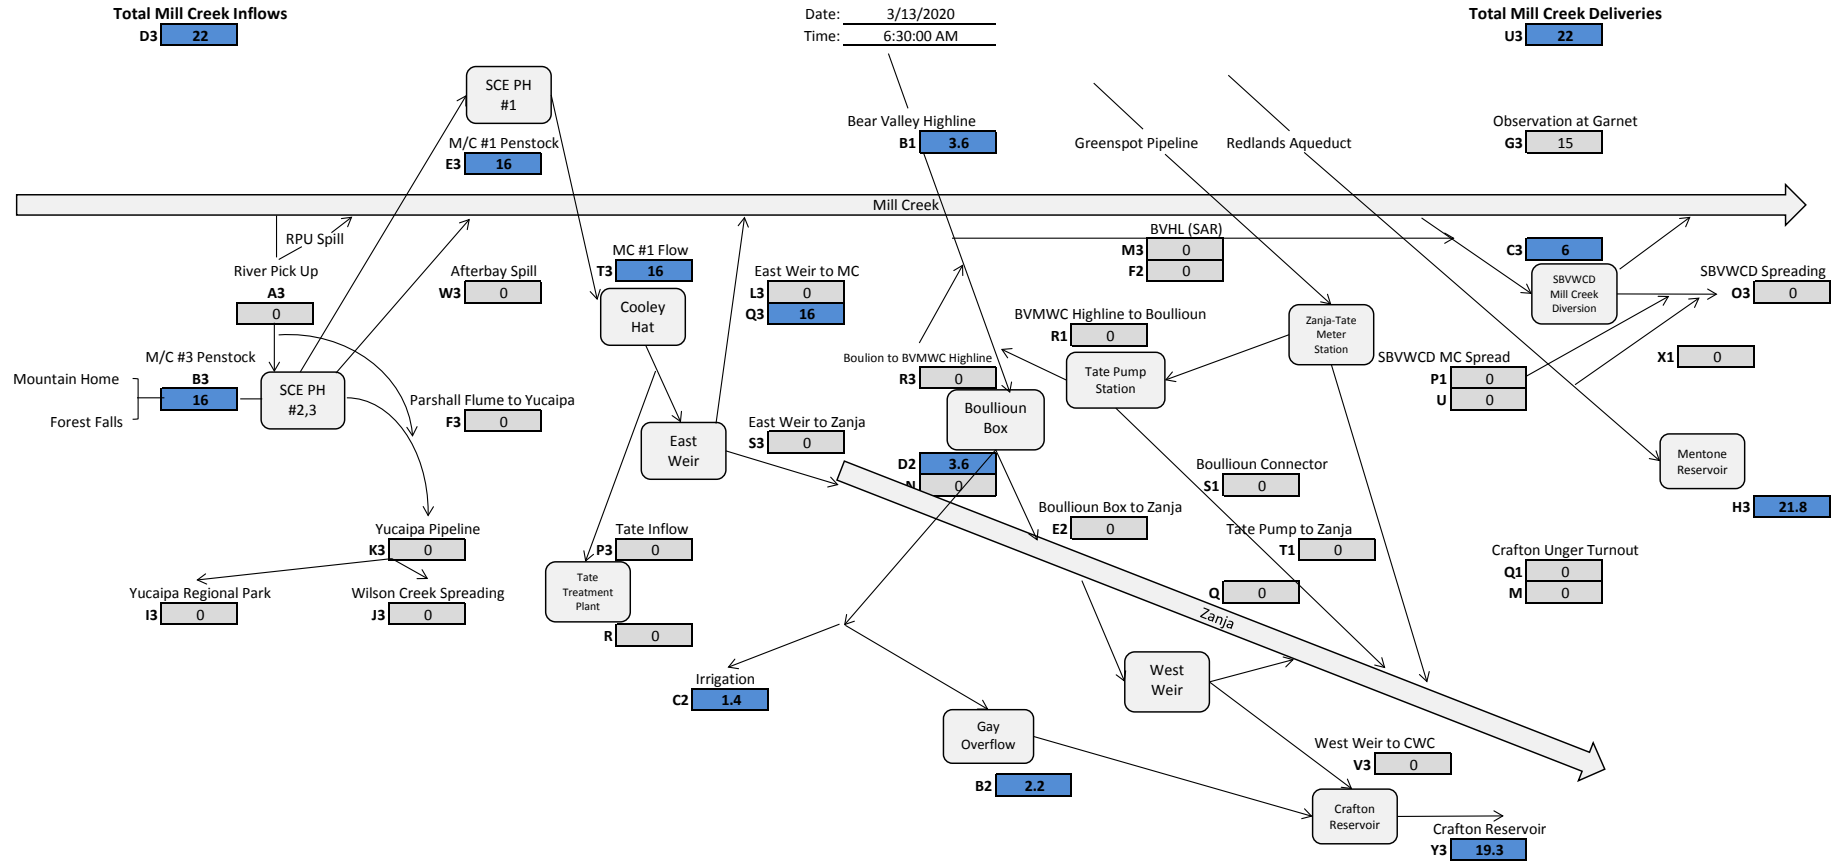

Santa Ana River - Mill Creek Cooperative Water Project

Santa Ana Stations

